

Work Order ID 147677

Wednesday, June 08, 2016 2:55:39 PM

147677

Page 1

Item ID: D6101-001 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Saddle Billet
 Start Date: 5/25/2016 Start Qty: 20.00 ***20*** Cust Item ID:
 Required Date: 6/8/2016 Req'd Qty: 20.00 ***20*** Customer:
 Reference: **DAS**

Approvals: Process Plan: **9-89** Date: **JUN 09 2016** Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D6101	Rev B

100	PURCHASING	0.00						DAS
100						<u>20</u>	<u>JUN 13 2016</u>	13
Purchasing	Memo	0.00						9-89
Purchasing	Issue P/O: <u>3267.4</u>							
	a) Description: Alluminum billet							
	b) 6.00" x 6.250" x 2.00" thick							
	c) Tolerance on length are +0.030"/-0.000" $\pm$ +/-0.008"							
	d) Grain direction along 6.00" length							
	e) Material: 7075-T7351 (QQ-A-250/12)							
	f) Material certification required							

110	Receive & Inspect for Damage & Mat'l Certs	0.00						
110								
Packaging	Memo	0.07						
Packaging	Ensure material certification is attached							

20x 8/16-7-19

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width:100%; border: none;"> <tr> <td style="border: none;">Skid-tube ☐</td> <td style="border: none;">Cross tube ☐</td> <td style="border: none;">Water Jet ☐</td> <td style="border: none;">Engineering ☐</td> </tr> <tr> <td style="border: none;">Machining ☐</td> <td style="border: none;">Small Fab ☐</td> <td style="border: none;">Prod. Eng. Coord. ☐</td> <td style="border: none;">Quality ☐</td> </tr> <tr> <td style="border: none;">Thermoforming ☐</td> <td style="border: none;">Finishing ☐</td> <td style="border: none;">Rec/Store/Packaging ☐</td> <td style="border: none;">Other ☐</td> </tr> <tr> <td style="border: none;">Large Fab ☐</td> <td style="border: none;">Composite ☐</td> <td style="border: none;">Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐																																															
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																																																																				
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																																																																				
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																																																																				
Large Fab ☐	Composite ☐	Supplier ☐																																																																					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval																																																																
Description Work Order Deviation				Disposition				Completed By																																																															
								Lead hand / Supervisor Approval Verification																																																															
								QC / QA Coordinator Approval																																																															
Root Cause <table style="width:100%; border: none;"> <tr><td style="border: none;">Environment ☐</td><td style="border: none;">No Re-verification ☐</td></tr> <tr><td style="border: none;">Design ☐</td><td style="border: none;">Operator ☐</td></tr> <tr><td style="border: none;">Doc/Data ☐</td><td style="border: none;">Offset/Setup ☐</td></tr> <tr><td style="border: none;">Equip/Tooling ☐</td><td style="border: none;">Supplier ☐</td></tr> <tr><td style="border: none;">Handling/Pre ☐</td><td style="border: none;">Training ☐</td></tr> <tr><td style="border: none;">Material ☐</td><td style="border: none;">Use for Testing ☐</td></tr> <tr><td style="border: none;">Internal Transport ☐</td><td style="border: none;">Poor Information ☐</td></tr> <tr><td style="border: none;">Tribal Knowledge ☐</td><td style="border: none;">Rushing ☐</td></tr> <tr><td style="border: none;">LOA ☐</td><td style="border: none;">Product Improvement ☐</td></tr> <tr><td style="border: none;">Substation ☐</td><td style="border: none;">Process Improvement ☐</td></tr> <tr><td style="border: none;">Past Expiry Date ☐</td><td style="border: none;">Manufacturing Process ☐</td></tr> <tr><td style="border: none;">Misidentified ☐</td><td style="border: none;">Past Due ☐</td></tr> </table>		Environment ☐	No Re-verification ☐	Design ☐	Operator ☐	Doc/Data ☐	Offset/Setup ☐	Equip/Tooling ☐	Supplier ☐	Handling/Pre ☐	Training ☐	Material ☐	Use for Testing ☐	Internal Transport ☐	Poor Information ☐	Tribal Knowledge ☐	Rushing ☐	LOA ☐	Product Improvement ☐	Substation ☐	Process Improvement ☐	Past Expiry Date ☐	Manufacturing Process ☐	Misidentified ☐	Past Due ☐	FAULT CATEGORY <table style="width:100%; border: none;"> <tr><td style="border: none;">Pressure/Forced ☐</td><td style="border: none;">Temperature/Cure ☐</td><td style="border: none;">Power Loss/Surge ☐</td><td style="border: none;">Positioned Wrong ☐</td></tr> <tr><td style="border: none;">Bending ☐</td><td style="border: none;">Set-up ☐</td><td style="border: none;">Folio/Program ☐</td><td style="border: none;">Outside Dimensions ☐</td></tr> <tr><td style="border: none;">Centre Not Concentric ☐</td><td style="border: none;">BOM/Route ☐</td><td style="border: none;">Grain ☐</td><td style="border: none;">Over/Under tolerance ☐</td></tr> <tr><td style="border: none;">Cracks ☐</td><td style="border: none;">Broken/Damage/Defect ☐</td><td style="border: none;">Weld ☐</td><td style="border: none;">Part Incorrect ☐</td></tr> <tr><td style="border: none;">Crimp/Kink/Ripple/Wave ☐</td><td style="border: none;">Inspection Incomplete/Unqualified ☐</td><td style="border: none;">Wrong Stock Pulled ☐</td><td style="border: none;">Part Lost/Missing ☐</td></tr> <tr><td style="border: none;">Cuffs ☐</td><td style="border: none;">Contamination ☐</td><td style="border: none;">Out of Sequence ☐</td><td style="border: none;">Part Moved ☐</td></tr> <tr><td style="border: none;">Crushing ☐</td><td style="border: none;">Countersink ☐</td><td style="border: none;">Off-set ☐</td><td style="border: none;">Drawing ☐</td></tr> <tr><td style="border: none;">Heat Treat ☐</td><td style="border: none;">Cut Too Short ☐</td><td style="border: none;">Mislabeled ☐</td><td style="border: none;">Finish ☐</td></tr> <tr><td style="border: none;">Wave/Twist in Tube ☐</td><td style="border: none;">Instructions Incomplete/Unclear ☐</td><td style="border: none;">Fit/Function ☐</td><td style="border: none;">Misread ☐</td></tr> <tr><td style="border: none;">Marks/Chatter ☐</td><td style="border: none;">Drill Holes ☐</td><td style="border: none;">Misaligned/off center ☐</td><td style="border: none;">Turning Sequence ☐</td></tr> </table>						Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐
Environment ☐	No Re-verification ☐																																																																						
Design ☐	Operator ☐																																																																						
Doc/Data ☐	Offset/Setup ☐																																																																						
Equip/Tooling ☐	Supplier ☐																																																																						
Handling/Pre ☐	Training ☐																																																																						
Material ☐	Use for Testing ☐																																																																						
Internal Transport ☐	Poor Information ☐																																																																						
Tribal Knowledge ☐	Rushing ☐																																																																						
LOA ☐	Product Improvement ☐																																																																						
Substation ☐	Process Improvement ☐																																																																						
Past Expiry Date ☐	Manufacturing Process ☐																																																																						
Misidentified ☐	Past Due ☐																																																																						
Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐																																																																				
Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐																																																																				
Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐																																																																				
Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐																																																																				
Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐																																																																				
Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐																																																																				
Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐																																																																				
Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐																																																																				
Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐																																																																				
Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐																																																																				
OTHER : _____																																																																							

Wednesday, June 08, 2016 2:55:39 PM

147677

Page 2

Accept

N900040100

Setup Start *NS1*

Stop *NS2*

Item Name: Saddle Billet

Start Date: 5/25/2016 **Start Qty:** 20.00

20

Cust Item ID:

Required Date: 6/8/2016 **Req'd Qty:** 20.00

20

Customer:

Reference:

Approvals: **Process Plan:** _____ **Date:** _____ **Tooling:** _____ **Date:** _____

Run Start *NR1*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

**Insp.
Stamp**

0.00

120

QC

Quality Control

Memo

0.00

Ensure Material certification comply to Dwg D

DAS
14
9-99

16/07/20

Identify as per dwg & Stock Location: MAT042 0.00

130

Packaging

Packaging

Memo

0.03

LOCATION: MAT042

DAS
14
9-89

16/07/25

QC21- Final Inspection - Work Order Release	0.00
---	------

140

QC

Quality Control

Memo

0.33

**DAS
21
9-89**

JUL 20 2016

dm 16/07/20

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval																																																									
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																									
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER :			
Misidentified ☐	Past Due ☐																																																																

Picklist Print

Wednesday, June 08, 2016 2:55:39 PM

Page 1
/

Work Order ID: 147677

147677

Parent Item: D6101-001

D6101-001

Parent Item Name: Saddle Billet

Start Date: 5/25/2016

Required Date: 6/8/2016

Start Qty: 20.00

Required Qty: 20.00

Comments: IPP B: 01.05.04New IssueEC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D6101-001P		Purchased	No			110	Each	0.0000	1	20			
D6101-001P									**				
7075-T7351 2X6X6.25													

DOX Sp/6-7-19

DQA: _____ Date: _____


**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
OTHER : ☐									

SPECIFICATION CONTROL DRAWING

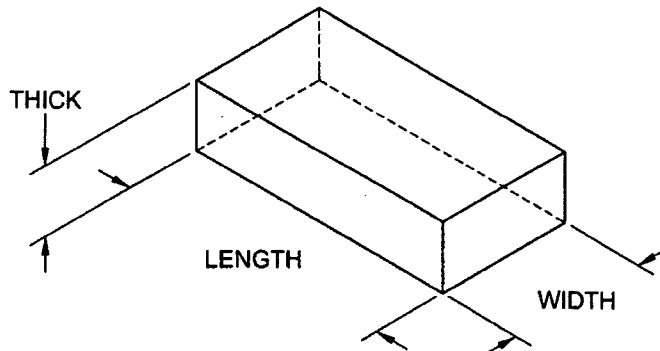

DAS
13
9-89

JUN 09 2016

W/O 147677

PURCHASE MATERIAL ACCORDING TO THE FOLLOWING TABLE. SPECIFY ALLOY, LENGTH x WIDTH x THICK (+0.030/-0.000), AND GRAIN DIRECTION AS SHOWN.

TOLERANCES ON ALL DIMENSIONS ARE +0.030/-0.000.

ALL DIMENSIONS ARE IN INCHES.

B ACCEPTABLE SPECIFICATIONS FOR 7075-T7351 ALUMINUM ARE AMS-QQ-A-250/12, QQ-A-250/12, OR ASTM B209

Part No.	Alloy	Length	Width	Thick	Grain Direction
D6101-001	7075-T7351 (QQ-A-250/12)	6.000	6.250	2.000	Along 6.000 Length
D6101-003	7075-T7351 (QQ-A-250/12)	7.875	6.250	2.000	Along 7.875 Length
D6101-005	7075-T7351 (QQ-A-250/12)	5.000	8.250	2.500	Along 5.000 Length
D6101-007	7075-T7351 (QQ-A-250/12)	7.750	8.250	2.500	Along 7.750 Length
D6101-009	7075-T7351 (QQ-A-250/12)	8.700	8.250	2.500	Along 8.700 Length
D6101-011	7075-T7351 (QQ-A-250/12)	9.700	8.250	2.500	Along 9.700 Length
D6101-013	7075-T7351 (QQ-A-250/12)	10.100	8.250	2.500	Along 10.10 Length
D6101-015	7075-T7351 (QQ-A-250/12)	9.450	6.250	2.500	Along 9.450 Length
D6101-017	7075-T7351 (QQ-A-250/12)	6.350	6.250	2.250	Along 6.350 Length

RELEASED
09/07/15/WP

B	ADDED D6101-015/-017, ADD ASTM B209	RF	09.04.23
A	NEW ISSUE	CP	01.03.30
REV.	DESCRIPTION	BY	DATE
DESIGN	CP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	RF		
CHECKED		DRAWING NO. REV. B	
MFG. APPR.		D6101 SHEET 1 OF 1	
APPROVED		TITLE SCALE	
DE APPR.		SADDLE BILLET, 7075 NTS	
DATE	09.04.23	COPYRIGHT © 2001 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID PO32674

Purchase Order Date 6/13/2016

PO Print Date 6/13/2016

Page Number 1 of 3

Order From :
METAUX CASTLE
P.O. BOX 4090 STN A
TORONTO, ONTARIO M5W OE9
CANADA

VU-MET002

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

E-MAILED
JUN 13 2016

Contact Name
Vendor Phone

Ship To Contact
Ship To Phone

Ship Via: Yours ppd
Ship Acct:

Buyer Chantal Lavoie
Customer POID
Customer Tax # 10127-2607
Terms Net 30
Currency USD
FOB Destination-Collect

Line Nbr	Reference Vendor Part Number Line Comments Delivery Comments	Description/ Mfg ID	Req Date/ Taxable Promise Date	CD	Req Qty/ Unit of Measure	PO Unit Price	Extended Price
1	D6101-001P	7075-T7351 2X6X6.25	6/28/2016 Yes 6/28/2016		20.00 Each	\$26.88	\$537.60
AS PER DWG D6101 REV. B B147677 SIZE: 6.00" X 6.250" X 2.00" THICK GRAIN DIRECTION ALONG 6.00" LENGHT MATERIAL: 7075-T7351 QQ-A-250/12 TOLERANCE AS PER QUOTE +.030"/-.000"							Line Total: \$537.60
2	D6101-003P	7075-T7351 2X6.25X7.875	6/28/2016 Yes 6/28/2016		30.00 Each	\$35.29	\$1,058.70
AS PER DWG D6101 REV. B B147659 SIZE: 7.875" X 6.250" X 2.00" THICK GRAIN DIRECTION ALONG 7.875" LENGHT MATERIAL: 7075-T7351 QQ-A-250/12 TOLERANCE AS PER QUOTE +.030"/-.000"							

Note:

6/13/2016

**Castle Metals®**

A. M. Castle & Co.

PACKING SLIP/
CERTIFICATE OF CONFORMANCE

Page 1 of 2

Shipment No:3027263

Ship From: A. M. CASTLE & CO. 2150 ARGENTIA ROAD MISSISSAUGA, ON L5N 2K7 CAN		Sold To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA		Ship To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CAN		Deliver To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA	
Date Shipped 18-JUL-16	F.O.B. ORIGIN	Freight Terms Prepaid		Carrier MANITOULIN		BOL No 3027263-2	

Shipment Details	Final Destination Branch - TOR
-------------------------	---------------------------------------

Order No 4393750	Line No 1	Item No 752237.MO	Description 2.0000.PL.7075.T7351.ALUMINUM.USI.48.5000.144.5000 CUT RECTANGLE TO 6.25 IN (+ .0310/- .0000 IN (GRAIN TO RUN ALONG 6")) X 6 IN (+ .0310/- .0000 IN (GRAIN TO RUN ALONG 6")) - ALUMINUM PLATE SAW SPECIFICATIONS: AMS-QQ-A-250/12				
Purchase Order No 32674		Part Number YOUR ITEM NUMBER: D6101-001		Ordered Qty 20.00 PCS		Invoice Qty 20.00 PCS	
Details		ALL PAPERWORK MUST FOLLOW ORDER / CUSTOMER MUST RECEIVE AT TIME OF DELIVERY ALL MATERIAL MUST HAVE IDENTIFYING MARKINGS EX:HEAT #'S Email P/s and certs to: clavoie@dartaero.com END USER: DART AEROSPACE END USE: COMMERCIAL AIRCRAFT PARTS SP 16-719					
Delivery No. 120481762	Mill KAISER ALUMINUM	Heat Number 	Mech Id	PCS 20	Width (IN)	Length (IN)	Shipped Qty(LBS) 154.8319

These commodities/technologies are subject to US Export Administration & US State Dept. Regulations and, if intended for export, were/are exported thereunder. Diversion contrary to US Law is Prohibited.

We hereby certify the material covered by this certification conforms in accordance with the above specifications and has been found to meet the applicable requirements for the material, including any specifications forming a part of the description. Test reports are on file subject to examination. All claims for defective material are waived unless made in writing to A.M. Castle & Co. within 60 days of the shipment. Material cut to the correct size, or material cut by the customer cannot be returned

These commodities, technology or software were exported from the United States in accordance with the Export Administration Regulations. Diversion contrary to US law prohibited.

Date Printed: 18-JUL-2016 05:25:25 PM



Castle Metals®

A. M. Castle & Co.

PACKING SLIP/
CERTIFICATE OF CONFORMANCE

Page 2 of 2

for credit.		
Reviewed by Authorized Castle Metals Representative:	Date:	Name:

Chris Galt

JUL 19 2016



Sp/6-7-19

SHIP TO:

A M CASTLE METALS
4175 ROYAL DRIVE, SUITE 600
KENNESAW, GA 30144

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

SOLD TO:

AM CASTLE & CO- SOLD TO
1420 KENSINGTON RD
SUITE 220
OAK BROOK, IL 60523

CERTIFIED TEST REPORT

Serial Number
4400333

CUSTOMER PO NUMBER: 344153		WORK PACKAGE:		CUSTOMER PART NUMBER: 752237		SHIP RUN/LOAD: 103411/15		GOV'T CONTRACT NUMBER:	
KAISER ORDER NO: 1199131	LINE ITEM: 1	SHIP DATE: 9-DEC-2015	ALLOY: 7075	CLAD: BARE	TEMPER: T7351	PRODUCT DESCRIPTION: KaiserSelect Plate			
WEIGHT SHIPPED: 5728 LB	QUANTITY: 4 PCS EST.	TRUCK B/L #: 2057457	GAUGE: 2.0000 IN (50.8000 MM)		DIAMETER/WIDTH: 48.500 IN (1231.9 MM)		LENGTH: 144.500 IN (3670.3 MM)		

MHU 1945251: LOT 153169B8: 3 pieces;
MHU 1954065: LOT 159084B3: 1 pieces;

Certified Specifications

DAS
14
9-89

16/07/20

AMS 4078/RevJ
ASTM B 209/Rev14
BSS 7055/RevB
DPS 4.713/RevAK
MMS 159/RevT

AMS-QQ-A-250/12/RevA
ASTM B 594/Rev13
CMMP 025/RevU
GAMPS 9101/RevB/AmdSCN1
PS 21211/RevM

AMS-STD-2154/RevA
BAC 5439/RevJ
CSTI 006/RevE
GSS16100/RevG/Amd1

Test Code: 4297

Test Results

Lot: 153169B8

Cast 885

Drop 18

Ingot 1

Melted in USA

(ASTM E8/B557)

(EN 2002-1)

Tensile:

Temper
T7351

Dir / # Tests
LT / 2 (Min:Max)

Ultimate KSI (MPA)
71.1 : 71.5
(490 : 493)

Yield KSI (MPA)
60.4 : 61.2
(416 : 422)

Elongation %
11.5 : 11.7

(ASTM E1004)

(EN 2004-1)

Conductivity %IACS : 40.3 Min
(MS/M) : 23.4 Min

41.2 Max
23.9 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.10	0.21	1.5	0.06	2.4	0.21	5.7	0.03	0.01	0.02	TOT 0.05

DEC 15 2015

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT

Serial Number
4400333

Lot: 159084B3 Cast 895 Drop 54 Ingot 2 Melted in USA

(ASTM E8/B557)
(EN 2002-1)

Tensile:	Temper	Dir / # Tests	Ultimate KSI (MPA)	Yield KSI (MPA)	Elongation %
	T7351	LT / 2 (Min:Max)	71.4 : 74.1 (492 : 511)	61.2 : 63.7 (422 : 439)	12.3 : 12.4

(ASTM E1004)
(EN 2004-1)
Conductivity %IACS : 39.7 Min
(MS/M) : 23.0 Min 40.9 Max
23.7 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.09	0.19	1.5	0.04	2.5	0.20	5.7	0.03	0.01	0.01	TOT 0.05

ALLOY LIMITS

7075	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER	MAX
MIN(wt%)	0.00	0.00	1.2	0.00	2.1	0.18	5.1	0.00	0.00	0.00	EACH	0.05
MAX(wt%)	0.40	0.50	2.0	0.30	2.9	0.28	6.1	0.20	0.05	0.05	TOT	0.15

Aluminum Remainder

ORDER COMMENTS

AMC CA-15413A R 7
AMS 4078,AMS QO-A-250/12,AMS STD-2154,A
STM B209,ASTM B594,BS
S 7055,CMMP 025,CSTI 006,DPS 4.713,GAMP
S 9101,MMS 159,PS 212

11

TEST NOTES

Metal represented by this test report was 100% immersion
ultrasonically tested from one side with 3mm dead zones top
and bottom and meets the Class A and Class B requirements of
all specifications referenced on this test report. No
surface marking of sonic indications is performed.

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT


Serial Number
4400333

CERTIFICATION

Kaiser Aluminum Fabricated Products, LLC (Kaiser), is ISO-9001:2008/AS9100C certified and hereby certifies that all material shipped under this order:

- has been inspected, tested, and found to be in conformance with the requirements of the specifications indicated herein. For material thicknesses outside specification limits, mechanical properties are as shown herein and chemical composition meets specification requirements.
- was melted in the United States of America or a qualifying country per DFARS 225.872-1(a), was manufactured in the United States of America, and meets the requirements of DFARS 252.225 for domestic content.
- has been thermally processed in compliance with AMS 2772, where applicable.
- is mercury free, within the limits of detection of ASTM E1251 (C = 1ppm).
- is in compliance with RoHS 2, European Union Directive 2011/65/EU.
- is in compliance with and regularly monitors any updates to the European Chemical Agency, ECHA, REACH regulations, (EC) n°1907/2006.
- is free of Conflict Minerals, as defined in Section 15.2 of the Dodd-Frank Act.

Any warranty is limited to that shown on Kaiser Aluminum's standard general terms and conditions of sale. Test reports are on file, subject to examination. Test reports shall not be reproduced except in full, without the written approval of the Kaiser Aluminum laboratory. The recording of false, fictitious or fraudulent statements or entries on the certificate may be punished as a felony under federal law.



JAMES HEMENWAY, LABORATORIES SUPERVISOR

SHIP TO:

A M CASTLE METALS
4175 ROYAL DRIVE, SUITE 600
KENNESAW, GA 30144

KAISER
ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT

Serial Number
4400333

SOLD TO:

AM CASTLE & CO- SOLD TO
1420 KENSINGTON RD
SUITE 220
OAK BROOK, IL 60523

CUSTOMER PO NUMBER: 344153		WORK PACKAGE:		CUSTOMER PART NUMBER: 752237		SHIP RUN/LOAD: 103411/15		GOV'T CONTRACT NUMBER:		
KAISER ORDER NO: 1199131		LINE ITEM: 1	SHIP DATE: 9-DEC-2015		ALLOY: 7075	CLAD: BARE	TEMPER: T7351	PRODUCT DESCRIPTION: KaiserSelect Plate		
WEIGHT SHIPPED: 5728 LB		QUANTITY: 4 PCS EST.		TRUCK B/L #: 2057457		GAUGE: 2.0000 IN (50.8000 MM)		DIAMETER/WIDTH: 48.500 IN (1231.9 MM)		LENGTH: 144.500 IN (3670.3 MM)

MHU 1945251: LOT 153169B8: 3 pieces;
MHU 1954065: LOT 159084B3: 1 pieces;

Certified Specifications

AMS 4078/RevJ
ASTM B 209/Rev14
BSS 7055/RevB
DPS 4.713/RevAK
MMS 159/RevT

AMS-QQ-A-250/12/RevA
ASTM B 594/Rev13
CMMP 025/RevU
GAMPS 9101/RevB/AmdSCN1
PS 21211/RevM

AMS-STD-2154/RevA
BAC 5439/RevJ
CSTI 006/RevE
GSS16100/RevG/Amd1

Test Code: 4297

Test Results

Lot: 153169B8 Cast 885 Drop 18 Ingot 1 Melted in USA

(ASTM E8/B557)
(EN 2002-1)

Tensile:	Temper	Dir / # Tests	Ultimate KSI (MPA)	Yield KSI (MPA)	Elongation %
	T7351	LT / 2 (Min:Max)	71.1 : 71.5 (490 : 493)	60.4 : 61.2 (416 : 422)	11.5 : 11.7

(ASTM E1004)
(EN 2004-1)

Conductivity %IACS :	40.3 Min	41.2 Max
(MS/M) :	23.4 Min	23.9 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.10	0.21	1.5	0.06	2.4	0.21	5.7	0.03	0.01	0.02	TOT 0.05

DEC 15 2015

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT

Serial Number
4400333

Lot: 159084B3 Cast 895 Drop 54 Ingot 2 Melted in USA

(ASTM E8/B557)
(EN 2002-1)

Tensile:	Temper	Dir / # Tests	Ultimate KSI (MPA)	Yield KSI (MPA)	Elongation %
	T7351	LT / 2 (Min:Max)	71.4 : 74.1 (492 : 511)	61.2 : 63.7 (422 : 439)	12.3 : 12.4

(ASTM E1004)
(EN 2004-1)
Conductivity %IACS : 39.7 Min
(MS/M) : 23.0 Min 40.9 Max
23.7 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.09	0.19	1.6	0.04	2.5	0.20	5.7	0.03	0.01	0.01	TOT 0.05

ALLOY LIMITS

7075	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER	MAX
MIN(wt%)	0.00	0.00	1.2	0.00	2.1	0.18	5.1	0.00	0.00	0.00	EACH	0.05
MAX(wt%)	0.40	0.50	2.0	0.30	2.9	0.28	6.1	0.20	0.05	0.05	TOT	0.15

Aluminum Remainder

ORDER COMMENTS

AMC CA-15413A R 7
AMS 4078,AMS QO-A-250/12,AMS STD-2154,A
STM B209,ASTM B594,BS
S 7055,CMMP 025,CSTI 006,DPS 4.713,GAMP
S 9101,MMS 159,PS 212

11

TEST NOTES

Metal represented by this test report was 100% immersion
ultrasonically tested from one side with 3mm dead zones top
and bottom and meets the Class A and Class B requirements of
all specifications referenced on this test report. No
surface marking of sonic indications is performed.

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT


Serial Number
4400333

CERTIFICATION

Kaiser Aluminum Fabricated Products, LLC (Kaiser), is ISO-9001:2008/AS9100C certified and hereby certifies that all material shipped under this order:

- has been inspected, tested, and found to be in conformance with the requirements of the specifications indicated herein. For material thicknesses outside specification limits, mechanical properties are as shown herein and chemical composition meets specification requirements.
- was melted in the United States of America or a qualifying country per DFARS 225.872-1(a), was manufactured in the United States of America, and meets the requirements of DFARS 252.225 for domestic content.
- has been thermally processed in compliance with AMS 2772, where applicable.
- is mercury free, within the limits of detection of ASTM E1251 (< 1 ppm).
- is in compliance with RoHS 2, European Union Directive 2011/65/EU.
- is in compliance with and regularly monitors any updates to the European Chemical Agency, ECHA, REACH regulations, (EC) n°1907/2006.
- is free of Conflict Minerals, as defined in Section 15.2 of the Dodd-Frank Act.

Any warranty is limited to that shown on Kaiser Aluminum's standard general terms and conditions of sale. Test reports are on file, subject to examination. Test reports shall not be reproduced except in full, without the written approval of the Kaiser Aluminum laboratory. The recording of false, fictitious or fraudulent statements or entries on this certificate may be punished as a felony under federal law.



JAMES HEMENWAY, LABORATORIES SUPERVISOR

MATERIAL RECEIPT INSPECTION FORM

PO / BATCH NO 32674/147677

MATERIAL D6101-001
DATE 16/07/20

MATERIAL CERT REQD yes
QUANTITY RECEIVED 20
QUANTITY INSPECTED 20
QUANTITY REJECTED _____

THICKNESS ORDERED 6.00X6.250X2.00
THICKNESS RECEIVED 6.00X6.250X2.00
SHEET SIZE ORDERED _____
SHEET SIZE RECEIVED _____

DESCRIPTION	NCR (Check Y/N)		COMMENTS
SURFACE DAMAGE	☒	☒	
CORRECT FINISH	☒	☒	
CORROSION	☒	☒	
CORRECT GRAIN DIRECTION	☒	☒	
CORRECT MATERIAL	☒	☒	
CORRECT THICKNESS	☒	☒	
PHOTO REQUIRED	☒	☒	
CORRECT MATERIAL	☒	☒	
CORRECT REF # TO LINK CERT	☒	☒	
CORRECT MATERIAL IDENTIFICATION	☒	☒	
CORRECT M# ON THE MATERIAL	☒	☒	
DOES THIS MATERIAL REQUIRE ENGINEERING SIGN OFF	☒	☒	
DOES THIS REQUIRE AN EXTRUSION REPORT	☒	☒	

CUT SAMPLE PIECE OF MATERIAL AND PERFORM A HARDNESS CHECK RECORD RESULTS BELOW				
TYPE OF MATERIAL	HRC	HRB	DUR A	DUR D
SIZE OF TEST SAMPLE				
HARDNESS / DUROMETER READING				

testers located in the Quality Office

QC 18 INSPECTION		ENGINEERING SIGNOFF (if required)	
INSPECTED BY _____	DATE <u>16/07/20</u>	SIGNED OFF BY _____	DATE _____

Attach this inspection sheet with the corresponding material cert and remit to be scanned and received in

MATERIAL RECEIPT INSPECTION FORM

INSTRUCTIONS FOR INSPECTING BAR, TUBING, ROUND, & SHEET STOCK

1. VERIFY STOCK TO DART PURCHASE ORDER
2. MEASURE ALL DIMENSIONS FOR EACH PURCHASED STOCK
 - a. WIDTH, THICKNESS DIAMETER WALL THICKNESS & LENGTH
3. VERIFY CONDITION OF MATERIAL (e.g. DAMAGED CORRODED ETC)
4. VERIFY THAT SUPPLIER HAS A NUMBER (HEAT #) ON ITS RECEIVING REPORT TO LINK TO MATERIAL CERT'S
5. VERIFY MATERIAL CERTS ARE CORRECT TO THE DART PO INSTRUCTIONS
6. REMOVE / CUT A PIECE OF MATERIAL FOR SAMPLE HARDNESS TESTING

INSTRUCTIONS FOR INSPECTING SKIDTUBE & STEP EXTRUSION

1. VERIFY TO DART SUPPLIED DRAWING
 2. SAMPLE INSPECT MATERIAL IN BUNDLE TO ENSURE MATERIAL CAN BE RECEIVED INTO DART
 3. USING PORTABLE HARDNESS TESTER VERIFY HARDNESS OF THE MATERIAL TO THE DRAWING
 4. VERIFY THAT MATERIAL CERT'S MATCH TO WHAT'S CALLED UP ON THE DART DRAWING
- AFTER MATERIAL PASSES INSPECTION**
5. HAVE DART EMPLOYEES START STOCKING MATERIAL BUT REQUEST MIN 20pcs FOR FULL INSPECTION
 6. INSPECT ALL DIMS AS PER DRAWING REQUIREMENTS

INSTRUCTIONS FOR INSPECTING CROSS TUBE MATERIAL

1. VERIFY MATERIAL CERT'S MATCH THE REQUIREMENTS ON THE DART DRAWINGS
2. INSPECT MIN HALF THE BATCH OF EXTRUSION RECEIVED INTO DART
3. INSPECT MATERIAL AS PER THE EXTRUSION REPORT
 - a. WALL THICKNESS USING ULTRA-SONIC IN 4 LOCATIONS
 - b. OUTSIDE DIAMETER HIGHEST/LOWEST BOTH ENDS
 - c. INSIDE DIAMETER HIGHEST/LOWEST BOTH ENDS
 - d. STRAIGHTNESS @ CENTER OVER 12" SPAN
 - e. WALL THICKNESS USING TUBE MICROMETER HIGHEST/LOWEST BOTH ENDS
4. IDENTIFY EACH TUBE IN SEQUENCE OF INSPECTING (TUBE 1, TUBE 2,) AND W/O# AND PO#
5. RECORD ALL FINDINGS ON EXTRUSION REPORT

IF ANY QUESTIONS PLEASE SEE OC COORDINATOR BEFORE GOING FURTHER
